



CITY OF BELLE ISLE, FLORIDA

CERTIFICATE OF OCCUPANCY

Date Issued: **October 7, 2020**
PERMIT#: **2020-02-060**
Name of Owner: **Hrkalovic, Aleksandar and Anita**

Certificate of Occupancy for the property located at 5205 Oak Island Road, Belle Isle, FL 32809, Parcel #18-23-30-7164-00-140. This property has been approved for use as a Single Family Residence/R-3.

The edition of the code which the permit was issued:	2017 Florida Building Code 6th Edition
The use and occupancy, in accordance with the provisions of Chapter 3:	Construction of a new SFR R-3
The type of construction as defined in Chapter 6:	VB
The design occupant load:	NA Residential
A description of the portion of the structure for which issued	Construction of Entire New SFR Structure
If an automatic sprinkler system required:	No
Is an automatic sprinkler system installed:	No
Any special stipulations/conditions of the building permit:	No

This structure as defined by the scope of the permit listed above has been inspected for compliance with the requirements of this code for the occupancy and division of occupancy and the use for which the proposed occupancy is classified.

It is unlawful to use this property except in the manner for which this certificate is intended. This Certificate provides that the above described property may lawfully be used in the manner for which it was intended and all inspections have been completed and satisfied by the City of Belle Isle Contract Building Official.

David Olivieri - Building Official

Date: 10.07.2020



STATE OF FLORIDA
DEPARTMENT OF HEALTH
ONSITE SEWAGE TREATMENT AND DISPOSAL SYSTEM
CONSTRUCTION INSPECTION AND FINAL APPROVAL

RECEIVED
OCT 07 2020

APPLICATION #: AP1474462
PERMIT #: 48-SX-2049198
DOCUMENT #: F1518496
DATE PAID: 06/05/2020
FEE PAID: 65.00
RECEIPT #: 48-PID-4441939

APPLICANT: Aleksander Hrkalovic
AGENT: Sauer Septic
PROPERTY ADDRESS: 5205 Oak Island Rd Orlando, FL 32809
LOT: 14 BLOCK:
SUBDIVISION: Pleasure Island ID#: 18-23-30-7164-00-140

CHECKED [X] ITEMS ARE NOT IN COMPLIANCE WITH STATUTE OR RULE AND MUST BE CORRECTED.

TANK INSTALLATION

[] [01] TANK SIZE [1] 1250.00 [2] _____
[] [02] TANK MATERIAL Polyethylene
[] [03] OUTLET DEVICE _____
[] [04] MULTI-CHAMBERED [Y / N]
[] [05] OUTLET FILTER Tuf-Tite dual EF-4
[] [06] LEGEND 1. 70-156-12DC3 2. _____
[] [07] WATERTIGHT
[] [08] LEVEL
[] [09] DEPTH TO LID

SETBACKS

[] [27] SURFACE WATER _____ FT
[] [28] DITCHES _____ FT
[] [29] PRIVATE WELLS _____ FT
[] [30] PUBLIC WELLS _____ FT
[] [31] IRRIGATION WELLS _____ FT
[] [32] POTABLE WATER 55 FT
[] [33] BUILDING FOUNDATIONS 5.5 FT
[] [34] PROPERTY LINES 24 FT
[] [35] OTHER _____ FT

DRAINFIELD INSTALLATION

[] [10] AREA [1] 585 Trench [2] _____ SQFT
[] [11] DISTRIBUTION BOX HEADER X
[] [12] NUMBER OF DRAINLINES 1. 5.00 2. _____
[] [13] DRAINLINE SEPARATION
[] [14] DRAINLINE SLOPE
[] [15] DEPTH OF COVER
[] [16] ELEVATION [ABOVE / BELOW] BM 48.00
[] [17] SYSTEM LOCATION
[] [18] DOSING PUMPS _____
[] [19] AGGREGATE SIZE
[] [20] AGGREGATE EXCESSIVE FINES
[] [21] AGGREGATE DEPTH

FILLED / MOUND SYSTEM

[] [36] DRAINFIELD COVER
[] [37] SHOULDERS
[] [38] SLOPES
[] [39] STABILIZATION _____

ADDITIONAL INFORMATION

[] [40] UNOBSTRUCTED AREA
[] [41] STORMWATER RUNOFF
[] [42] ALARMS
[] [43] MAINTENANCE AGREEMENT
[] [44] BUILDING AREA
[] [45] LOCATION CONFORMS WITH SITE PLAN
[] [46] FINAL SITE GRADING
[] [47] CONTRACTOR Darrell Clay (Sauer Septic Sy
[] [48] OTHER ADS Septic Stack-9 (9 pipes - 2 tier)

ABANDONMENT

[] [49] TANK PUMPED _____
[] [50] TANK CRUSHED & FILLED

Comments: Comments are on page 2.

CONSTRUCTION [APPROVED / DISAPPROVED]: Orange CHD DATE: 06/05/2020
Environmental Specialist II Drake D Brown (Florida Department of Health)

FINAL SYSTEM [APPROVED / DISAPPROVED]: Orange CHD DATE: 10/06/2020
Environmental Specialist II Drake D Brown (Florida Department of Health)

(Explanation of Violations on following page)

DH 4016, 08/09 (Obsoletes all previous editions which may not be used)
Incorporated: 64E-6.003, FAC



STATE OF FLORIDA
DEPARTMENT OF HEALTH
ONSITE SEWAGE TREATMENT AND DISPOSAL SYSTEM
CONSTRUCTION INSPECTION AND FINAL APPROVAL

APPLICATION #: AP1474462
PERMIT #: 48-SX-2049198
DOCUMENT #: F11518496
DATE PAID: 06/05/2020
FEE PAID: 65.00
RECEIPT #: 48-PID-4441939

<u>Violation Number</u>	<u>Comment</u>

Comments

Re-inspection fee paid 10/6/20
Re-inspection by DB 10/5/20
Re-inspection fee not paid
Watertight, water line, unobstructed area and building area: Okay
BM: 16 BDF: 64 Soils: Okay
4L x 40'; 1L x 35'
no visible retention areas.
The system is sized for 4 bedrooms with a maximum occupancy of 8 persons (2 per bedroom), for a total estimated flow of 460 gpd.



City of Belle Isle

Universal Engineering Sciences 3532 Maggie Blvd., Orlando, FL 32811
Tel 407-581-8161 * Fax 407-581-0313 * www.universalengineering.com

APPLICATION FOR CERTIFICATE OF OCCUPANCY/COMPLETION

APPLICANT SHALL PROVIDE A COPY OF THE FINAL INSPECTION CARD. FAILURE TO DO SO WILL DELAY YOUR APPLICATION REQUEST.

I am applying for a certificate of Occupancy \$50.00 Completion \$50.00

DATE: 8/28/20

BLDG PERMIT # 2020-02-060 Scope of Work NEW CONSTRUCTION HOUSE

Project Address 5205 OAK ISLAND RD. BELLE ISLE, FL 32809

Property Owner ALEKSANDAR HRKALOVIC Contact No. 407-690-9334

Contractor OWNER BULD Contact No. 407-690-9334

Contractor Address 1123 WALTHAM AVE ORLANDO FL 32805 License No. _____

PLEASE COMPLETE AND SIGN BELOW

2017 FBC 6th Edition
The edition of the FL building code which the permit was issued.

100% entire structure
A description of the portion of the structure for which issued.

TYPE 5 VB
The type of construction as defined in FBC, Ch. 6, Sec. 602

N/A REQUIRED
If an automatic sprinkler system is provided, whether it is required.

SINGLE FAMILY RESIDENTIAL SFR
The use and occupancy, in accordance with the provisions of FBC, Ch. 3, Sec. 301

N/A
Any special stipulations/conditions of the building permit.

N/A
The design occupant load.

Have there been any name or other major changes to this project
YES NO

Prior to the issuance of a Certificate of Occupancy/Completion for the above referenced building or part thereof, the undersigned contractor by signing below does hereby certify that he/she personally supervised the construction of the above mentioned building or part thereof and that said building or part thereof has been constructed in all respects in compliance with the Building Code, all other City ordinances and regulations relating to the above mentioned project and in accordance with the plans and specifications as approved by the City of Belle Isle and does hereby assume complete responsibility for the construction thereof.

Contractor Signature: _____

Certificate of Occupancy and Permanent Electrical Service

It is the responsibility of the Contractor to schedule and obtain approved plumbing, mechanical, electrical, fire, engineering and building inspections as required, including final inspections prior to the issuance of the Certificate of Occupancy and the connection of permanent electrical service.

Certificate of Completion

A certificate of completion will be issued, upon request, for completed alterations to structures already occupied and accessory structures, such as fences and utility buildings.

Paid: Cash/Check# 9539 Date: 10-2-20 Rec'd By: [Signature]
VISA

Written request for a certificate may be made via FAX to 407-581-0313 or EMAIL at BIDPermits@universalengineering.com



Inspection Report

10/2/2020 3:00:19 PM

Project: 2020-02-060 bldg permit new SFR

Address: City of Belle Isle, 5205 Oak Island Road, Belle Isle, FL 32809

2020-02-060	Results	Date	Inspector	License
COBI - CODE 130 Slab Inspection	Pass	03/27/2020	Bernard Elkins	
COBI - CODE 140 Lintel/Tie Beam Inspection	Fail	04/07/2020	Bernard Elkins	
COBI - CODE 140 Lintel/Tie Beam Inspection	Pass	04/08/2020	Bernard Elkins	
COBI - CODE 170 Window In-Progress Inspection	Pass	06/04/2020	Leslie S. Rutherford	
COBI - CODE 180 Sheathing (wall) Inspection	Pass	04/20/2020	Leslie S. Rutherford	
COBI - CODE 190 Sheathing (roof) Inspection	Pass	04/20/2020	Leslie S. Rutherford	
COBI - CODE 195 Dry-In Inspection (roof & walls)	Pass	04/24/2020	Leslie S. Rutherford	
COBI - CODE 200 Frame Inspection	Pass	06/11/2020	Leslie S. Rutherford	
COBI - CODE 205 Drywall Nail/Screw Inspection	Pass	06/23/2020	Bernard Elkins	
COBI - CODE 230 Insulation Inspection	Partial	06/19/2020	David M. Olivieri	
COBI - CODE 240 Lathe Inspection	Pass	06/22/2020	Bernard Elkins	



10/2/2020 3:00:19 PM

Project: 2020-02-060 bldg permit new SFR

Address: City of Belle Isle, 5205 Oak Island Road, Belle Isle, FL 32809

REVIEW bldg app for new SFR	Pass	03/03/2020	Benjamin Suriel	
REVIEW revision to energy calcs to change to spray foam insulation on new SFR to change partial pass to full pass on inspection report	Pass	09/29/2020	David M. Olivieri	
2020-02-061	Results	Date	Inspector	License
COBI - CODE 195 Dry-In Inspection (roof & walls)	Pass	04/22/2020	Leslie S. Rutherford	
● COBI - CODE 720 Roof Final Inspection	Pass	06/04/2020	Leslie S. Rutherford	
REVIEW plumbing app for new SFR	Pass	03/03/2020	Benjamin Suriel	
REVIEW roof app for new SFR	Pass	03/03/2020	Benjamin Suriel	
2020-02-062	Results	Date	Inspector	License
COBI - CODE 610 Plumbing Underground Inspection	Pass	03/20/2020	Leslie S. Rutherford	
COBI - CODE 620 Plumbing Rough Inspection	Pass	05/22/2020	Leslie S. Rutherford	
2020-02-063	Results	Date	Inspector	License
COBI - CODE 320 Electrical Underground Inspection	Pass	03/26/2020	William P. Dasher	
COBI - CODE 330 Electrical Rough Inspection	Pass	06/11/2020	Leslie S. Rutherford	
REVIEW electrical app for new SFR	Pass	03/03/2020	Benjamin Suriel	



Inspection Report

10/2/2020 3:00:19 PM

Project: 2020-02-060 bldg permit new SFR

Address: City of Belle Isle, 5205 Oak Island Road, Belle Isle, FL 32809

COBI - CODE 840 Pool Rough/Underground Electrical Inspection	Pass	07/30/2020	Leslie S. Rutherford	
BUILDING - POOL 2020-05-047	Results	Date	Inspector	License
CODE 820 Pool Safety Inspection	Pass	09/23/2020	Leslie S. Rutherford	BN4564
• CODE 830 Final Pool Building Inspection		10/02/2020	Leslie S. Rutherford	BN4564
BUILDING 2020-02-060	Results	Date	Inspector	License
• CODE 250 Building Final Inspection	Pass	09/28/2020	Leslie S. Rutherford	BN4564
ELECTRICAL - POOL 2020-05-049	Results	Date	Inspector	License
CODE 860 Final Pool Electrical Inspection	Pass	09/22/2020	Leslie S. Rutherford	BN4564
ELECTRICAL 2020-02-063	Results	Date	Inspector	License
CODE 360 PrePower Inspection	Pass	09/04/2020	William P. Dasher	BN4118
• CODE 380 Electrical Final Inspection	Pass	09/28/2020	Leslie S. Rutherford	BN4564
ELECTRICAL 2020-03-039	Results	Date	Inspector	License
• CODE 375 Electrical Low Voltage Final Inspection	Pass	09/25/2020	Leslie S. Rutherford	BN4564

10/2/2020 3:00:19 PM

Inspection Report

Project: 2020-02-060 bldg permit new SFR

Address: City of Belle Isle, 5205 Oak Island Road, Belle Isle, FL 32809

2020-03-035	Results	Date	Inspector	License
COBI - CODE 300 Temp Pole Inspection	Pass	04/27/2020	William P. Dasher	
2020-05-046	Results	Date	Inspector	License
COBI - CODE 510 Mechanical Rough Inspection	Pass	05/27/2020	Leslie S. Rutherford	
COBI - CODE 520 Hood Vent Inspection	Pass	06/12/2020	David M. Olivieri	
2020-05-047	Results	Date	Inspector	License
COBI - CODE 800 Pool Steel & Ground Inspection	Pass	07/15/2020	Leslie S. Rutherford	
2020-05-048	Results	Date	Inspector	License
COBI - CODE 870 Pool Rough/Underground Plumbing Inspection	Pass	07/15/2020	Leslie S. Rutherford	
COBI - CODE 870 Pool Rough/Underground Plumbing Inspection	Pass	07/30/2020	Leslie S. Rutherford	
2020-05-049	Results	Date	Inspector	License
COBI - CODE 840 Pool Rough/Underground Electrical Inspection	Pass	07/15/2020	Leslie S. Rutherford	



Inspection Report

10/2/2020 3:00:19 PM

Project: 2020-02-060 bldg permit new SFR


Address: City of Belle Isle, 5205 Oak Island Road, Belle Isle, FL 32809

MECHANICAL 2020-05-046	Results	Date	Inspector	License
● CODE 530 Mechanical Final Inspection	Pass	09/22/2020	Leslie S. Rutherford	BN4564
PLUMBING - POOL 2020-05-048	Results	Date	Inspector	License
CODE 880 Final Pool Plumbing Inspection	Pass	09/22/2020	Leslie S. Rutherford	BN4564
PLUMBING 2020-02-062	Results	Date	Inspector	License
● CODE 640 Irrigation Final Inspection	Pass	09/22/2020	Leslie S. Rutherford	BN4564
● CODE 650 Plumbing Final Inspection	Pass	09/25/2020	Leslie S. Rutherford	BN4564

10/2/2020 3:00:19 PM

Blower Door Form

Section 1

2017 6th ed Florida Building Code-Energy Testing	
Blower Door Test Form	
Builder	Hrkalovic Homes LLC
Builder Abbreviation	HH
Community	Belle Isle
Lot #	5205
Address	5205 Oak Island Road
Unit, If applicable	NA
City	Belle Isle
State	Florida
Zip	32809
Building Department Jurisdiction	City Of Belle Isle
Permit #	B2020-02-060
Front Of House Pic	

Blower Door Test Results

ACH(50) Specified On Calcs	4
Method for calculating building volume	Code software calculated
Building Volume	16736
CFM50 Test Results	765

Blower Door Form

ACH50	2.7
Pic of Blower Door Setup	 A photograph showing a blower door setup in a doorway. The door is open to the right. A red fabric enclosure is set up in the doorway, with a circular fan unit at the bottom. A white light fixture is suspended in the center of the enclosure. A control panel is visible on the left side of the enclosure. The room to the right of the door is brightly lit, while the room to the left is dark.

Blower Door Form



Pic of Blower Door Manometer



Deficiencies


Deficiency #1	
Deficiency #1 Recommendation	
Deficiency #1 Picture	
Deficiency #2	
Deficiency #2 Recommendation	
Deficiency #2 Picture	
Deficiency #3	
Deficiency #3 Recommendation	
Deficiency #3 Picture	

Blower Door Form

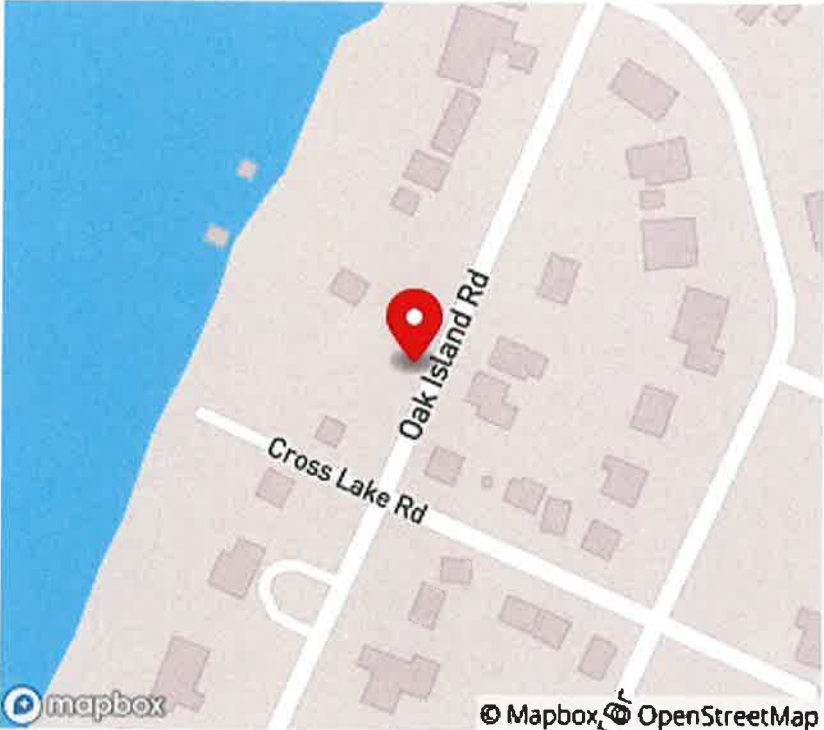
Deficiency #4 Picture	
Inspection Results	
Date/Time	09-23-2020
Infiltration Results	PASS (with Mechanical Ventilation)
Overall Inspection	PASS
Location / GPS	
	Lat: 28.4870571 Long: -81.352401
Field Tech Initials	G.M
Rater / RFI Name	George Malcolm
Rater Certification #	4639711
Signature	

Blower Door Form

Blower Door Certificate


 Orange County Division of Building Safety
 Building Inspection Section
 Permit No: 82022-02-000


Blower Door Test Form
For Prescriptive and Performance Method

Job Information	
Builder: <u>Hrkalovic Homes LLC</u>	Lot #: <u>5205</u>
Address: <u>5205 Oak Island Road</u>	
City, State, Zip: <u>Belle Isle, Florida 32809</u>	
Air Infiltration Test Results	
ACH(50) = CFM(50) X 60 / Volume = <u>2.7</u>	
<input type="checkbox"/> PASS (Mechanical Ventilation not Required) <input checked="" type="checkbox"/> PASS (With Mechanical Ventilation) <input type="checkbox"/> FAIL	
Certification of Test Results	
Please mark type of certification entity.	
<input checked="" type="checkbox"/> Energy Auditor or Energy Rater as defined in Florida Statutes Section 583.993. Copy of Certificates must be attached to this form. <input type="checkbox"/> Class A air-conditioning contractor, Class B air-conditioning contractor, or Mechanical Contractor. <input type="checkbox"/> Professional Engineer or Architect licensed by Florida Statutes Section 471 or 481.	
I hereby certify that the above Air Infiltration Test results demonstrate compliance with Florida Energy Code requirements in accordance with the Florida Building Code-Energy Conservation.	
Signature: <u></u>	Date: <u>09 / 23 / 2020</u>
Printed Name: <u>George Malcolm</u>	
Company: <u>APLUS RATING LLC</u>	License or Certification #: <u>4638711</u>

(NOTE: Completed Form to be submitted at final Building Inspection.)


Blower Door Form

Rater Certificate

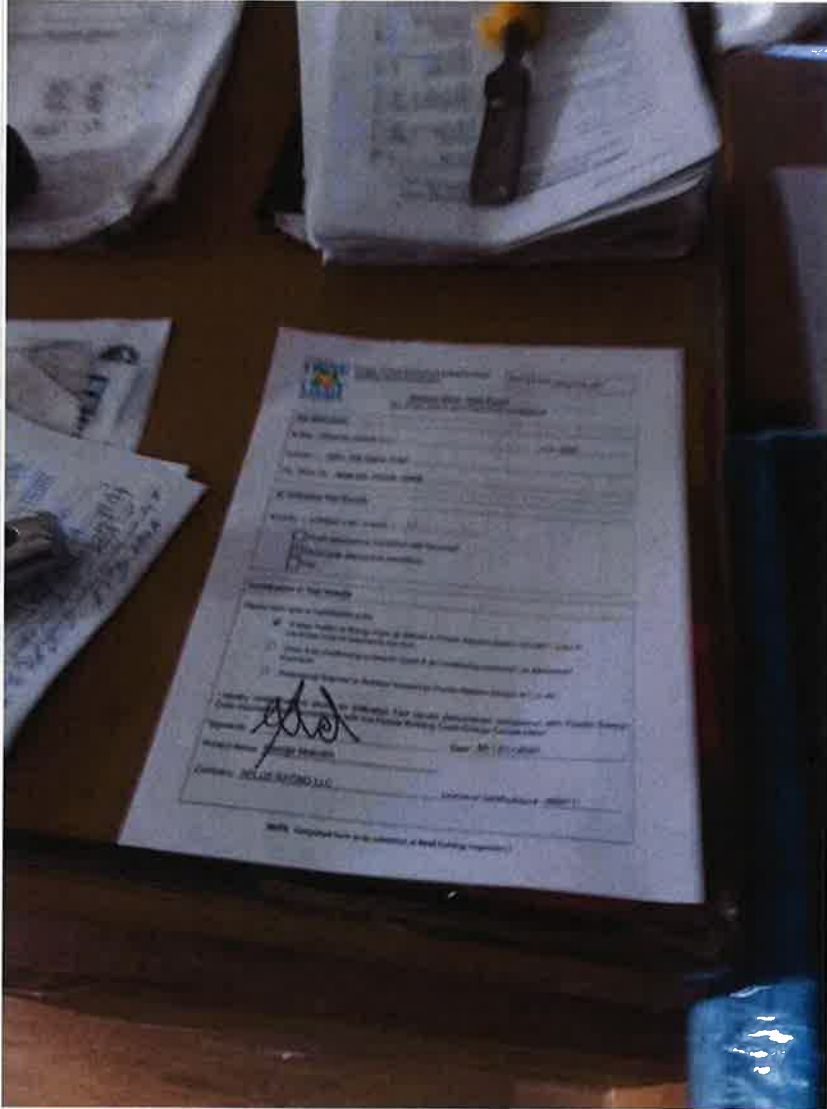

Blower Door Form

Rater Certificate

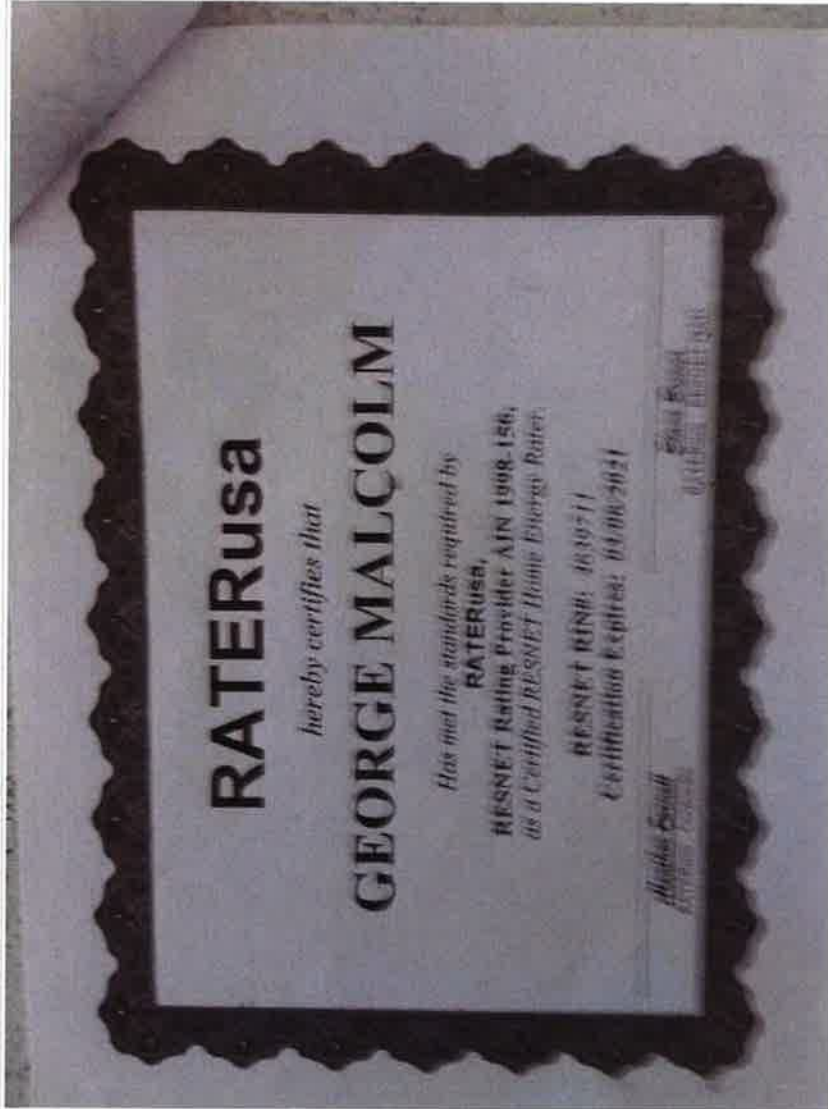

 **RICK SINGH, CFA - ORANGE COUNTY PROPERTY APPRAISER**

- [🔍 Searches](#)
- [🔍 Sales Search](#)
- [📄 Results](#)
- [📄 Property Record Card](#)
- [🔖 My Favorites](#)

[Sign up for e-Notify...](#)

5205 Oak Island Rd < 18-23-30-7164-00-140 >

Name(s)	Physical Street Address
Hrkalovic Aleksandar	5205 Oak Island Rd
Hrkalovic Anita	Postal City and Zipcode
Property Name	Orlando, Fl 32809
N/A. Click information icon to contribute.	Property Use
Mailing Address On File	0001 - Vacant Residential
1129 Waltham Ave	Municipality
Orlando, FL 32809-4249	Belle Isle
Incorrect Mailing Address?	



View 2020 Property Record Card

- [Property Features](#)
- [Values, Exemptions and Taxes](#)
- [Sales Analysis](#)
- [Location Info](#)
- [Market Stats](#)
- [🔄 Update Information](#)

Property Description

[View Plat](#)

REPLAT PLEASURE ISLAND H/71 LOT 14

Total Land Area 9,375 sqft (+/-) | 0.22 acres (+/-) [GIS Calculated](#) [Notice](#)

Land

Land Use Code	Zoning	Land Units	Unit Price	Land Value	Class Unit Price	Class Value
0001 - Vacant Residential	R-1-A	1 LOT(S)	\$95,000.00	\$95,000	\$0.00	\$95,000

Page 1 of 1 (1 total records)

Buildings

Important Information	Structure
There are no buildings associated with this parcel.	

Extra Features

FINAL SURVEY

LEGAL DESCRIPTION:

LOT 14, REPLAT OF PLEASURE ISLAND, ACCORDING TO THE PLAT THEREOF, AS RECORDED IN PLAT BOOK H, PAGE 71, OF THE PUBLIC RECORDS OF ORANGE COUNTY, FLORIDA.

FLOOD INFORMATION:

BY PERFORMING A SEARCH WITH THE LOCAL GOVERNING MUNICIPALITY OR WWW.FEMA.GOV, THE PROPERTY APPEARS TO BE LOCATED IN ZONE X. THIS PROPERTY WAS FOUND IN CITY OF BELLE ISLE, COMMUNITY NUMBER 120181, DATED 9/25/2009.


CERTIFIED TO:

C COMINS DEVELOPMENT



5205 OAK ISLAND RD, BELLE ISLE, FLORIDA 32809

- Wood Power Pole
- Water Meter
- Cleanout

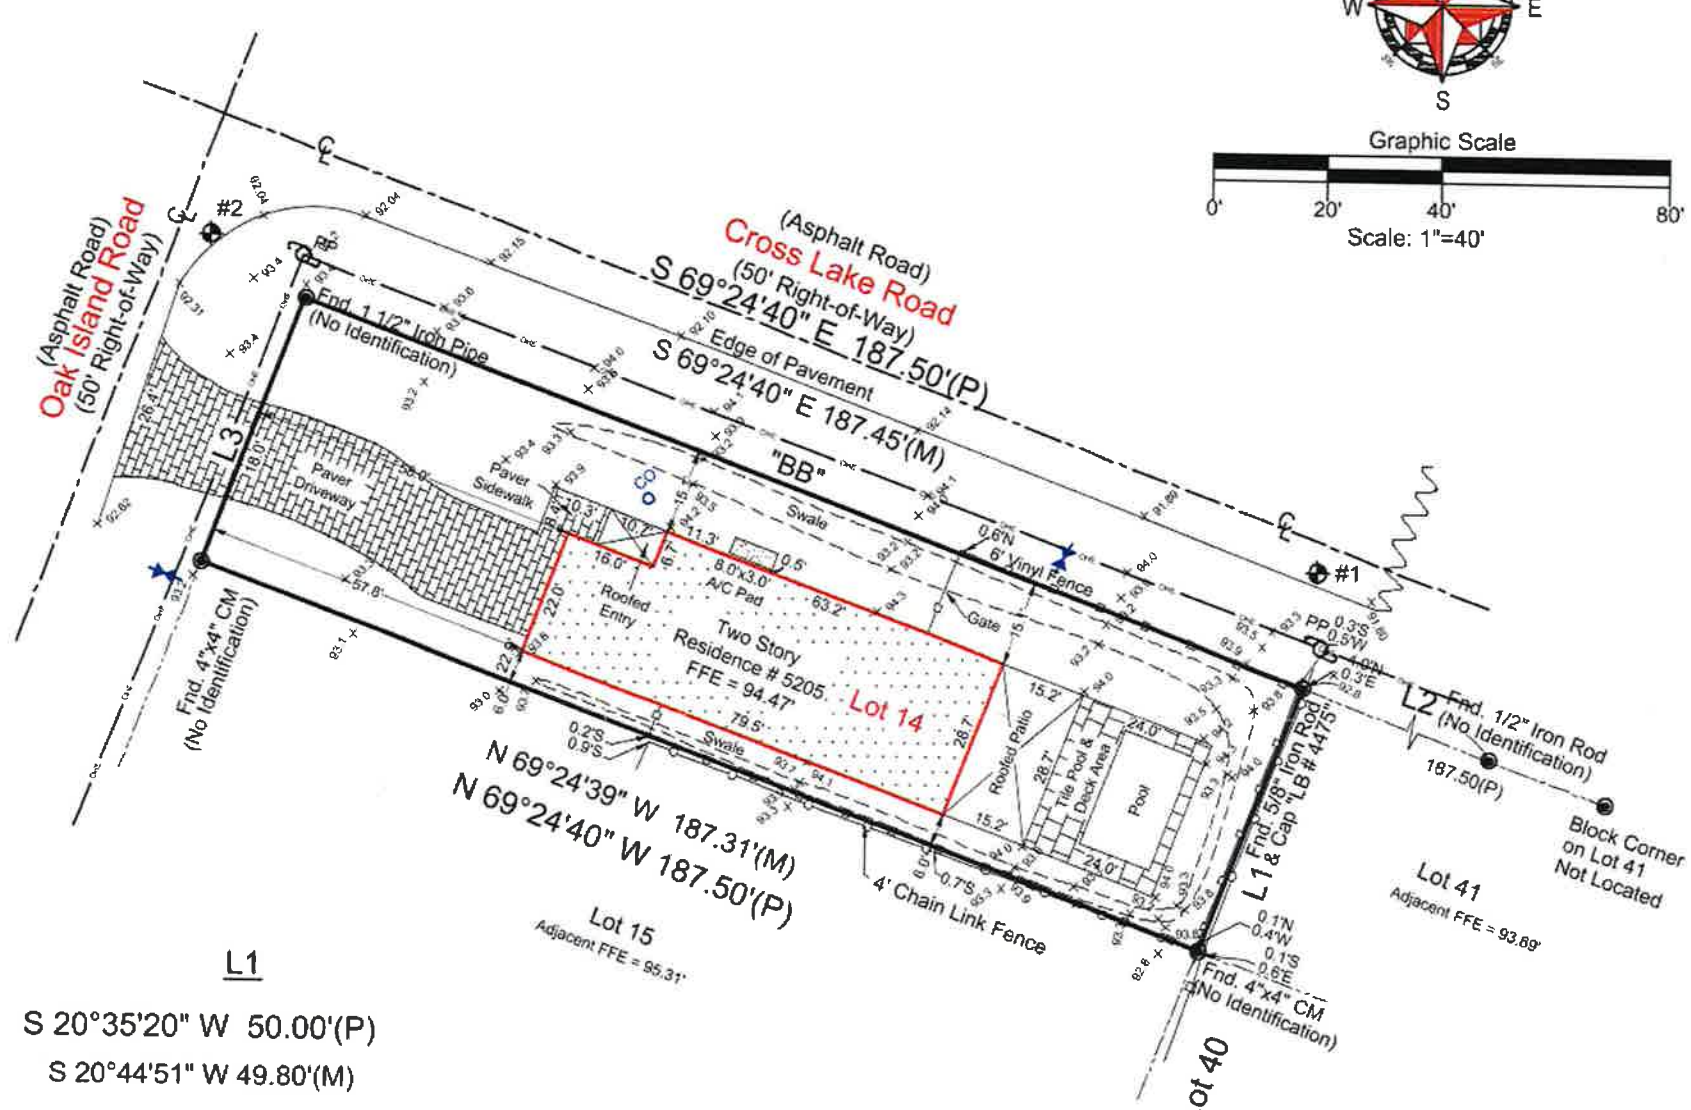

- L1**
 S 20°35'20" W 50.00'(P)
 S 20°44'51" W 49.80'(M)
- L2**
 S 69°24'40" E 122.50(D)
 S 69°27'37" E 122.69'(M)
- L3**
 N 20°35'20" E 50.00'(P)
 N 20°35'20" E 49.80'(M)

- Site Benchmark Information-**
- #1**
Set Nail & Disk LB# 7623 in Asphalt.
Elevation: 91.92'
 - #2**
Set Nail & Disk LB# 7623 in Asphalt.
Elevation: 92.20'

-Benchmark Information-
 F.D.o.T. GPS Network
 Florida Department of Transportation GPS Network.
 (Elevations are based upon NAVD 88 Datum)

Update: Revised Fences - 09/24/20 - ADS
 Update: Final Survey - 09/17/20 - TCD
 Update: Foundation Survey - 03/28/20 - TCD
 Update: Add Topo 08/15/18
 Original Survey: 06/24/16

Field Date: 9/23/2020 Date Completed: 09/21/20
 Drawn By: C.W. File Number: JS-29369 F1

-Legend-

C - Calculated	PC - Point of Curvature
CB - Centerline	Pg - Page
CM - Concrete Block	PI - Point of Intersection
Conc - Concrete	P.O.B. - Point of Beginning
D - Description	P.O.L. - Point on Line
DE - Drainage Easement	PP - Power Pole
Esmt. - Easement	PRM - Permanent Reference Monument
F.E.M.A. - Federal Emergency Management Agency	PT - Point of Tangency
FFE - Finished Floor Elevation	R - Radius
Fnd. - Found	Rad. - Radial
IP - Iron Pipe	R&C - Rebar & Cap
L - Length (Arc)	Rec. - Recovered
M - Measured	Rfd. - Roofed
N&D - Nail & Disk	Set - Set 1/2" Rebar & Cap "LB 7623"
N.R. - Non-Radial	Typ - Typical
ORB - Official Records Book	UE - Utility Easement
P - Plat	WM - Water Meter
P.B. - Plat Book	Δ - Delta (Central Angle)
□ - Wood Fence	-O- - Chain Link Fence

-NOTES-

- >Survey is Based upon the Legal Description Supplied by Client.
- >Abutting Properties Deeds have NOT been Researched for Gaps, Overlaps and/or Hiatu.
- >Subject to any Easements and/or Restrictions of Record.
- >Bearing basis shown hereon, is Assumed and Based upon the Line Denoted with a "BB".
- >Fence Ownership is NOT determined.
- >Roof Overhangs, Underground Utilities and/or Footers have NOT been located UNLESS otherwise noted.
- >Septic Tanks and/or Drainfield locations are approximate and MUST be verified by appropriate Utility Location Companies.
- >Use of This Survey for Purposes other than Intended, Without Written Verification, Will be at the User's Sole Risk and Without Liability to the Surveyor. Nothing Hereon shall be construed to give ANY Rights or Benefits to Anyone Other than those Certified.

-POINTS OF INTEREST-
 NONE VISIBLE

I hereby Certify that this Boundary Survey of the above Described Property is True and Correct to the Best of my Knowledge and Belief as recently Surveyed under my Direction on the Date Shown, Based on Information furnished to Me as Noted and Conforms to the Standards of Practice for Land Surveying in the State of Florida in accordance with Chapter 5J-17.052 Florida Administrative Codes, Pursuant to Section 472.027 Florida Statutes.

Patrick K. Ireland
 Patrick K. Ireland, P.S.M. #6637, LB 7623
 This Survey is intended ONLY for the use of Said Certified Parties.
 This Survey NOT VALID UNLESS signed and Embossed with Surveyor's Seal.

Ireland & Associates Surveying, Inc.
 800 Currency Circle | Suite 1020
 Lake Mary, Florida 32746
 www.irelandsurveying.com
 Office-407.678.3366 Fax-407.320.8165
